TR–25A LIFT DATA SHEET:

VERIFY POWER SUPPLY BELOW: CHOOSE ONE OF EACH

☐ 208-220/230 VAC	☐ 1 PHASE	☐ 60 HZ	STANDARD
☐ 440-460/480 VAC	☐ 3 PHASE	☐ 50 HZ	
☐ OTHER			

IF OTHER, STATE VOLTAGE ____VAC ___HZ

NOTE: NON-STANDARD OPTION MAY RESULT IN AN UPCHARGE

TRACK LENGTH: CHOOSE ONE

☐ 16'9"	☐ 20'	☐ 25'	☐ 30'	____OTHER (SPECIAL)

ABOVE IS NOT TIP-TO-TIP LENGTH, SEE LIFT DIMENSIONS BELOW

APPROACH RAMP LENGTH

☐ 5' STANDARD	____OTHER (SPECIAL)

AVAILABLE OPTIONS (*at additional cost*)

ELECTRIC/HYDRAULIC JACKING BEAM *(48" INSIDE TRACKS)*

☐ RJ–15 (15,000 LBS) ___QTY ☐ RJ–25 (25,000 LBS) ___QTY

ROLLING JACKING PLATFORM *(48" INSIDE TRACKS)*

☐ JP-15 (15,000 LBS) ___ QTY ☐ JP-25 (25,000 LBS) ___QTY

☐ SPECIAL WIDTH JACKING PLATFORM ___" (MIN 18" MAX 48")

☐ DRIVE THRU RAMPS – ADDS TO STANDARD LENGTH

☐ LED LIGHTS IN TRACKS

☐ ALIGNMENT CUTOUTS IN TRACKS

(*MUST RECEIVE TURNTABLE FROM CUST.*)

BRAND _____

MODEL # _____

☐ OIL DRAIN PAN *(48" INSIDE TRACKS ONLY)*

☐ EXTRA BASE PLATES FOR SHIMMING (1/2" THICK)

___ QTY × $ _____ EACH = TOTAL OF $_____

☐ CUSTOM WIDTH CROSSRAILS

(MIN 66" MAX 147") REQUEST

NOTE: CUSTOM WIDTH WILL RESULT IN AN UPCHARGE

WITH TRACKS ☐ CENTERED ☐ LEFT ☐ RIGHT ___"

☐ 3' EXTENSIONS (SET OF 2) – ADDS TO STANDARD LENGTH

☐ FRONT ☐ REAR ☐ BOTH

☐ 120 VAC DUPLEX OUTLET AT POWER UNIT

☐ THREE BEAM TRACK CONSTRUCTION

NOTE: SOME COMBINATIONS ARE NOT COMPATIBLE

PLEASE INITIAL THAT THE ABOVE SELECTIONS ARE CORRECT

_____

CUST. INITIAL

STANDARD

LIFT DIMENSIONS	**16'9"**	**20'**	**25'**	**30'**
LENGTH W/O RAMP:	219 3/4"	258 3/4"	318 3/4"	378 3/4"
LENGTH WITH RAMP:	288 1/16"	327 1/16"	387 1/16"	447 1/16"
WIDTH:	150 3/16"			
HEIGHT:	101 1/2"			

SLOPE IN FLOOR (LENGTHWISE) _____

SLOPE IN FLOOR (WIDTHWISE) _____

OVERHEAD OBSTRUCTIONS ☐ YES ☐ NO

IF YES, EXPLAIN _____

CONCRETE FLOOR MIN.: **4.5 IN. THICK; 4,000 PSI**

PLEASE INITIAL THAT THE ABOVE SELECTIONS ARE CORRECT

_____

CUST. INITIAL

PLEASE CHOOSE AN ORIENTATION (A, B, C, OR D) FOR POWER UNIT, TOPRAIL WILL BE LOCATED ON THE SAME SIDE AS THE POWER UNIT.

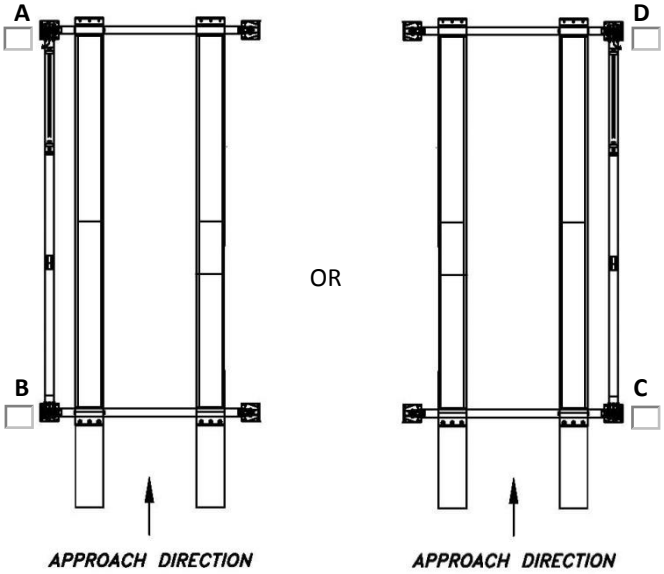

_____

CUST. INITIAL

POWER AND AIR FEEDS:

FINAL ELECTRICAL CONNECTION IS THE RESPONSIBILITY OF THE ELECTRICAL CONTRACTOR, MORE THAN ONE POINT OF CONNECTION MAY BE REQUIRED. DISCONNECT SWITCHES, MAIN FUSES, MAIN POWER LEADS, ETC. ARE NOT PROVIDED BY MOHAWK RESOURCES LTD.

PNEUMATIC POWER IS THE RESPONSIBILITY OF THE MECHANICAL CONTRACTOR TO THE FINAL DESIGNATED POINT OR POINTS AT THE VEHICLE LIFT UNLESS OTHERWISE SPECIFIED BY ARCHITECT.

VEHICLE DATA FORMS:

PROVIDE INFORMATION ON ATTACHED VEHICLE DATA FORMS (OR PROVIDE SKETCH WITH DIMENSIONS OF VEHICLE IF THE FORM DOES NOT PROPERLY REFLECT VEHICLE TYPE) FOR VEHICLES INTENDED TO BE SERVICED ON THIS LIFT. THIS IS TO ENSURE THAT THE VEHICLES WILL HAVE NO DIFFICULTY GETTING ON THE LIFT AND THAT THE LIFT WILL HAVE NO DIFFICULTY RAISING THE VEHICLES IN THE SPACE PROVIDED.

PROVIDE DETAILS ON ANY FEATURES OF THE VEHICLES THAT ARE OF CONCERN. THIS WILL ASSIST IN REVIEWING UNDER-VEHICLE CLEARANCE OVER RAMPS, BUMPER CLEARANCE APPROACHING RAMPS, REAR END DRAG CLEARANCE OVER RAMPS, OVERHEAD CLEARANCE WHEN FULLY RAISED, WHEEL BASE LENGTH OVER TRACK LENGTH, ETC…

ALL LIFT OPTIONS CHECKED FOR PURCHASE MUST BE LISTED ON PURCHASE ORDER AS SEPARATE LINE ITEMS.

I CHOOSE NOT TO COMPLETE DATA SHEETS* _____

CUST. INITIAL

IF NO DATA SHEETS ARE PROVIDED, MOHAWK TAKES NO RESPONSIBILITY FOR INCOMPATIBILITY WITH FACILITY OR TRUCKS/FORKLIFTS AND PAYMENT TERMS ARE 25% DOWN, REMAINDER BEFORE SHIPPING

CUSTOMER NAME:
CONTACT:
PHONE NUMBER:

CUSTOMER SIGNATURE _____ DATE _____
